

# MONTHLY PROGRESS REPORT



## **PRIME RESIDENCIES WRENDALE**

No 270, Sri Jayawardanapura MV,  
Rajagiriya.

**March – 2017**

## PROJECT DETAILS

<b>Project Architect</b> : Mr.AnilKumarage	<b>Contractor</b> : ACCESS CIVIMECH (Pvt) Ltd
<b>Structural Engineer:</b> Eng, Mr. Laksiri Cooray	<b>Project Commenced Date</b> – 2016/04/28
<b>MEP Engineer</b> : Eng, Mr. K. P. A. Weerasinghe	<b>Duration</b> – 20 Months
<b>Expected Date of Completion</b> : 2018/01/07	

## CURRENT STATUS OF THE PROJECT

Columns on the 5 <sup>th</sup> Floor	100% Completed
6 <sup>th</sup> floor slab concrete	100% Completed
Columns on the 6 <sup>th</sup> Floor	60% Completed
2 <sup>nd</sup> Floor Brick work	100% Completed
2 <sup>nd</sup> Floor Conduit placing & Wiring	100% Completed
2 <sup>nd</sup> Floor Internal Plaster	40% Completed
3 <sup>rd</sup> floor Brick work	80% Completed
3 <sup>rd</sup> Floor Conduit placing & Wiring	40% Completed
3 <sup>rd</sup> floor Internal Plaster	Started
4 <sup>th</sup> floor Brick work	30% Completed
1 <sup>st</sup> floor Painting work	Started





**Front view**



**Side view**




**Column concret @ 5<sup>th</sup> floor**



**Casting 6<sup>th</sup> floor slab**



**Column formwork @ 6<sup>th</sup> f**

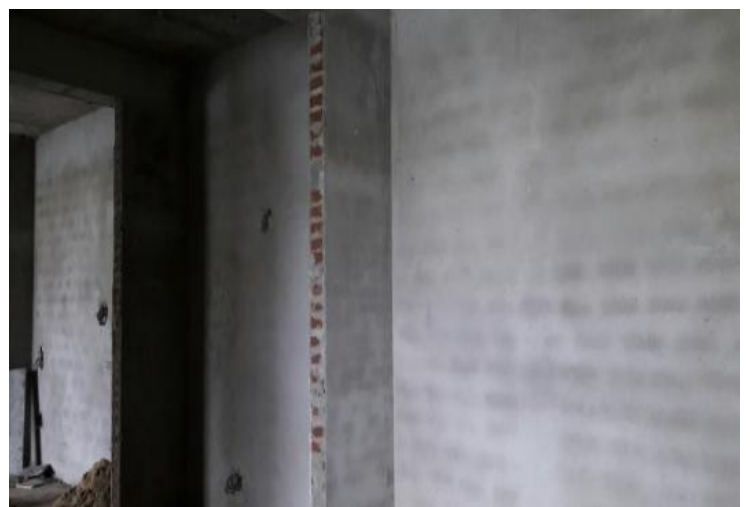

**Internal Plaster @ 2<sup>nd</sup> floor**





**Casting 6<sup>th</sup> floor**



**Wiring @ 2<sup>nd</sup> floor**




**Painting @ 1<sup>st</sup> floor**



**Brick work & plaster @ g.f**



**Brick work @ 3<sup>rd</sup> floor**

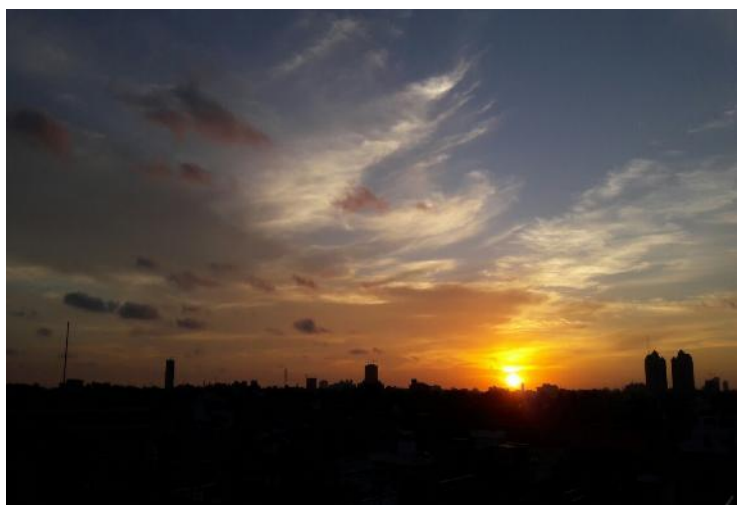

**Sun set from 4<sup>th</sup> floor**
