

MONTHLY PROGRESS REPORT

PRIME RESIDENCIES WATTALA
No 4, Gunasekara MW, Wattala, Mahabage.

March/ 2019



PROJECT DETAILS

Project Architect : Anil Kumarage, Chartered Architect	Contractor : PA Construction (PVT) Ltd
Structural Engineer : Eng. Laksiri Cooray	Project Commenced Date – 2016/06/29
MEP Engineer : Eng. K. P. A. Weerasinghe	Duration – 20 Months
Expected Date of Completion : 2018/02/18	

CURRENT STATUS OF THE PROJECT

Item No	Description	Progress Up to this Month		
		Block 01 (%)	Block 02 (%)	Block 03 (%)
1.0	Foundation work – Sub Structure	100	100	100
2.0	Superstructure	100	100	100
3.0	Masonry Work	100	100	100
4.0	Painting Work	100	100	100
5.0	Waterproofing Work	100	100	100
6.0	Tiling (Bathroom)	100	100	100
7.0	Tiling Work (Excl. Bathrooms)	100	100	100
8.0	Aluminium Works	100	100	100
9.0	Metal work	100	100	100
10.0	MEP Work (Electrical)	100	100	100
11.0	Plumbing Works	100	100	100
12.0	Fire			
12.1	Detection System	95	95	95
12.2	Protection System	100	100	100
13.0	Gas	100	100	100
14.0	Lift Installation	100	100	100
15.0	Pantry Cupboard Installation	100	100	100
16.0	Landscaping	80	80	80
17.0	Ground Preparation	100	100	100

CURRENT STATUS OF THE PROJECT
PROJECT COMPLETED & READY FOR HANDING OVER



Figure 1.1: Front view



Figure 1.2: Rear view



Figure 1.3: Building Entrance



Figure 1.4: Car parking Area



Figure 1.5: House Ready for Handover

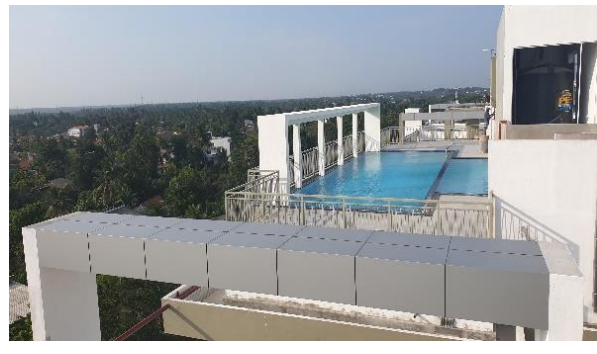


Figure 1.6: Swimming pool
