



PROPOSED APARTMENT COMPLEX AT No. 43, KASSAPA ROAD,
COLOMBO 05

KASSAPA II

Report

MONTHLY PROGRESS REPORT

January 2019



1. Project Details

Developer : Prime Residencies (Pvt) Ltd.

Project Architect : Arch Anil Kumarage

Structural Engineer : Laksiri Coorey

MEP Engineer : Kujana Weerasinghe

Contractor : K D Piling

Project Commencement : 1st January 2019

Current Status : Piling Phase

2. Project Progress

Table 01 – Pile Progress

Pile Diameter (mm)	Total Number of Piles	Completed	%
600	09	04	45 %
750	23	05	22 %
800	19	00	-
900	03	01	33 %

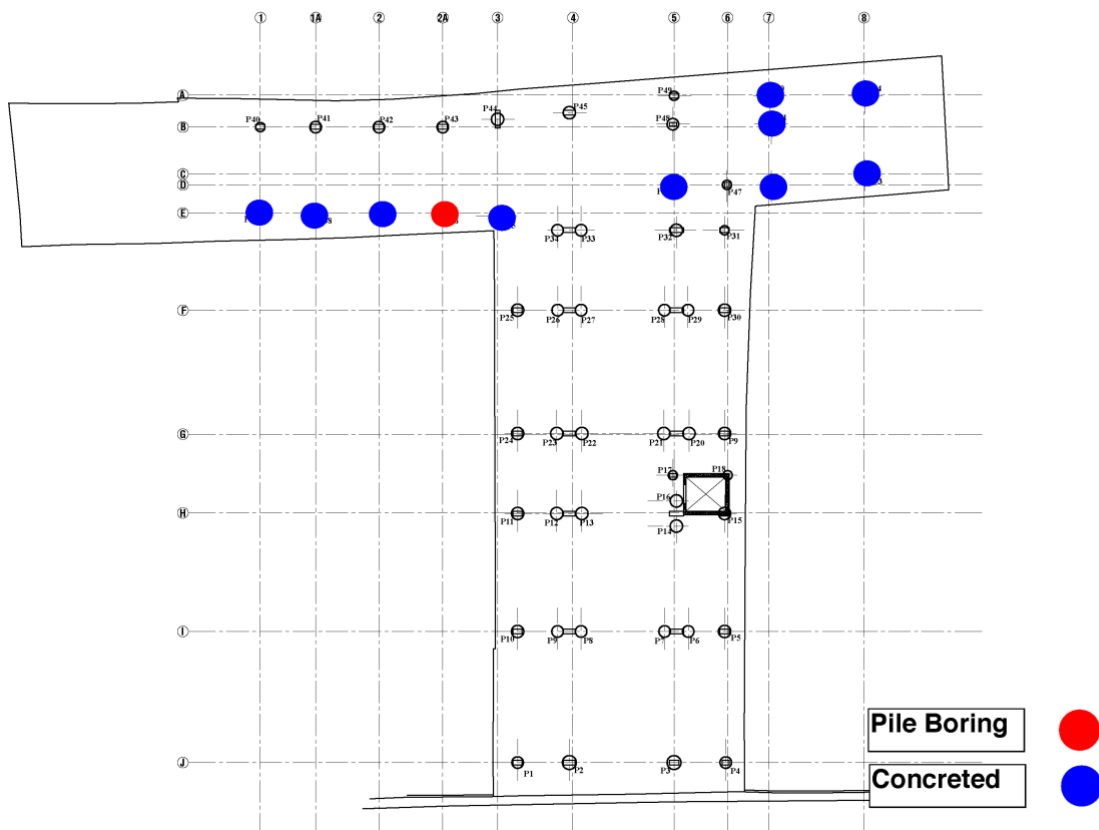


Figure 01 – Graphical representation of pile progress

3. Site Photographs



Figure 02 – Pile Boring



Figure 03 – Rebar Fabrication



Figure 03 – Pile Concreting



Figure 03 – Pile Boring
