



PROPOSED APARTMENT COMPLEX AT No. 43, KASSAPA ROAD,  
COLOMBO 05

## KASSAPA II

Report

### MONTHLY PROGRESS REPORT

March 2019



## **1. Project Details**

Developer : Prime Residencies (Pvt) Ltd.

Project Architect : Arch Anil Kumarage

Structural Engineer : Laksiri Coorey

MEP Engineer : Kujana Weerasinghe

Contractor : K D Piling


Project Commencement : 1<sup>st</sup> January 2019

Current Status : Piling Phase

## 2. Project Progress

**Table 01 – Pile Progress**

Pile Diameter (mm)	Total Number of Piles	Completed	%
600	09	09	100 %
750	23	23	100 %
800	19	12	63 %
900	03	01	33 %

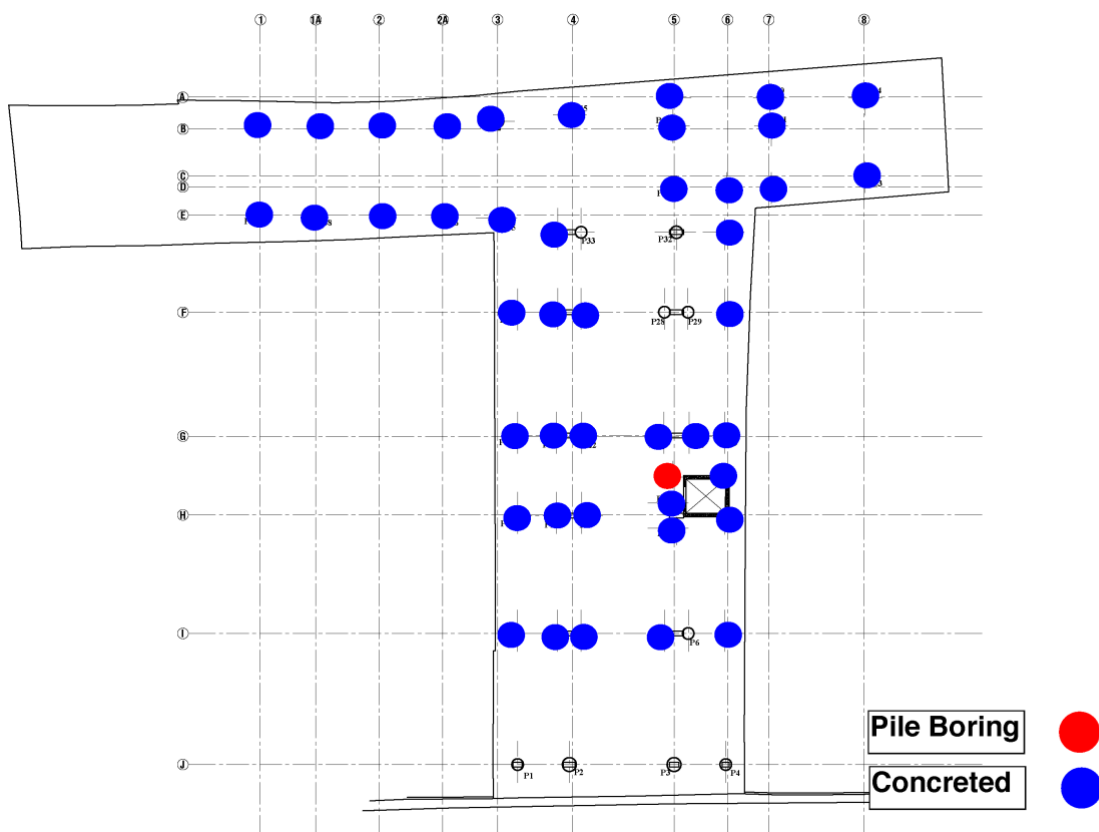

**Figure 01 – Graphical representation of pile progress**

### 3. Site Photographs



**Figure 02 – Pile Boring**



**Figure 03 – Site View**





**Figure 03 – Pile Concreting**



**Figure 03 – Pile Concreting**
