

MONTHLY PROGRESS REPORT

PRIME RESIDENCIES 298

No 298, High level Road. Colombo 06.

March / 2017



MONTHLY PROGRESS REPORT- March 2017

PROJECT DETAILS

Project Architect : Anil Kumarage, Chartered Architect	Contractor : ABC (Pvt) Ltd
Structural Engineer : Eng. Laksiri Cooray	Project Commenced Date – 24/02/2015
MEP Engineer : Eng. K. P. A. Weerasinghe	Duration – 22 Months
Expected Date of Completion : 24/05/2017	

CURRENT STATUS OF THE PROJECT

External Painting	100%
Hand rails	95 %
Fire & Gas work	80%
Internal Painting	80 %
Door window work	80%
Plumbing line	75 %
Boundary wall & gates	80%

PROJECT PICTURE

MONTHLY PROGRESS REPORT- March 2017



Front View



Side View

PROJECT PICTURES




Lift wall tiling



Swimming Pool Tiling

PROJECT PICTURES

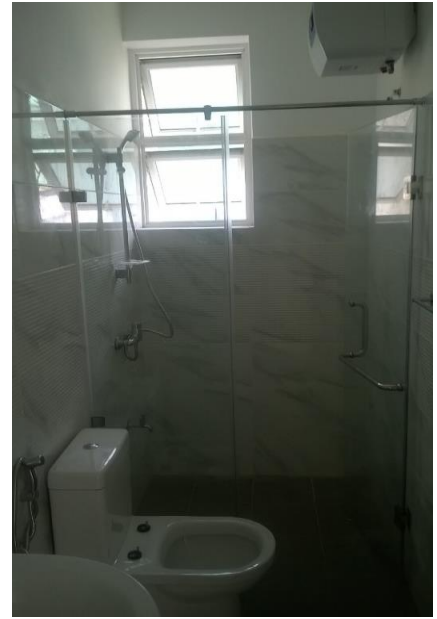

Bathroom Finishes



Final Painting



Pantry cupboards fixing



Front fence work WIP



Gas room construction WIP
